



Total Tasks	Done	Remainig Days	Finish Variance	Activity Status(Online)	On Time	Delayed	In Progress	planned	Actual	Urgent	project Name	Date	Name	Activity Status
63	29	24	-21	Delayed	15	26	46	1404/06/30	1404/06/30	14	All	All	All	All
Count of Activity Name by Activity Status				Average of Efficiency by Resource Name				Count of Activity Name by Resource Name						

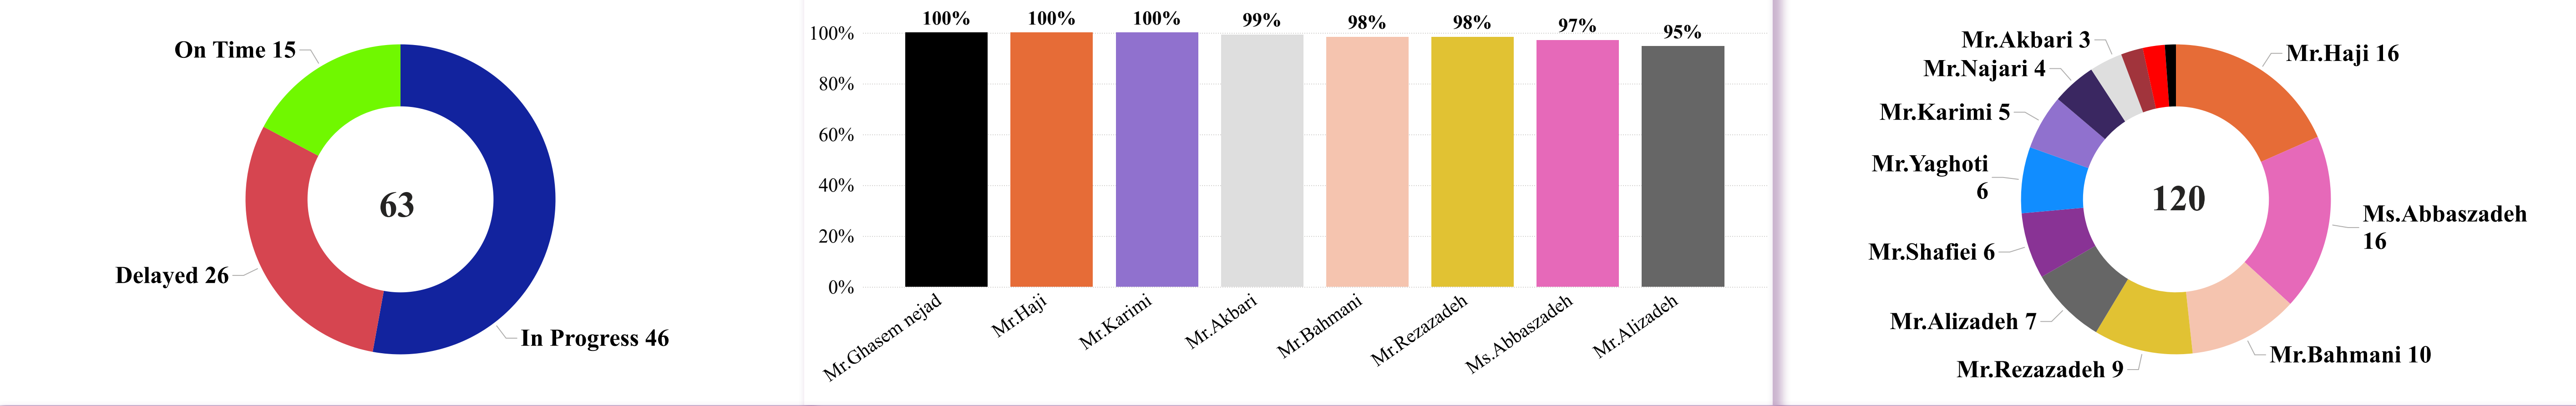

Activity Status	Activity Name	Resource Name	Planned_	Actual_	Remaining	Today	Delay Days	Head	Urgent
In Progress	طرح دوباره کاری	Mr.Abdollahi	1404/08/10		13	1404/07/27 15:35:33	0		
In Progress	لیست دوباره کاری	Mr.Abdollahi	1404/08/10		13	1404/07/27 15:35:33	0		
On Time	طرح بسته بندی	Mr.Akbari	1404/07/15	1404/07/13	-12	1404/07/27 15:35:33	0		
Delayed	طرح بسته بندی	Mr.Akbari	1404/07/20	1404/07/21	-7	1404/07/27 15:35:33	1		
Delayed	گزارش بازرسی ابعادی و چشمی	Mr.Akbari	1404/07/20	1404/07/21	-7	1404/07/27 15:35:33	1		
Delayed	مجموعه میانی و انتهایی OPC	Mr.Alizadeh	1404/07/07	1404/07/10	-20	1404/07/27 15:35:33	3		جلسه فوری
Delayed	منبع انتهایی OPC اصلاح	Mr.Alizadeh	1404/07/23	1404/07/26	-4	1404/07/27 15:35:33	3		جلسه فوری
Delayed	OPC بررسی و بروز رسانی	Mr.Alizadeh	1404/07/26		-1	1404/07/27 15:35:33	1		
Delayed	تهیه تجهیزات لیست تولیدی	Mr.Alizadeh	1404/07/15		-12	1404/07/27 15:35:33	12		جلسه فوری
In Progress	لیست تجهیزات تولیدی	Mr.Alizadeh	1404/07/30		3	1404/07/27 15:35:33	0		
In Progress	لیست تجهیزات تولیدی	Mr.Alizadeh	1404/08/05		8	1404/07/27 15:35:33	0		
Delayed	لیست تجهیزات، ماشین آلات و قالب‌های تولید	Mr.Alizadeh	1404/07/15	1404/07/23	-12	1404/07/27 15:35:33	8		جلسه فوری
Delayed	BOM	Mr.Bahmani	1404/07/07	1404/07/08	-20	1404/07/27 15:35:33	1		
Delayed	Data sheet	Mr.Bahmani	1404/07/20	1404/07/22	-7	1404/07/27 15:35:33	2		
Delayed	JES	Mr.Bahmani	1404/07/20	1404/07/22	-7	1404/07/27 15:35:33	2		
Delayed	دستورالعمل کار با فیکسچر کنترلی (اپراتور)	Mr.Bahmani	1404/07/20		-7	1404/07/27 15:35:33	7		جلسه فوری
Delayed	طرح دوباره کاری	Mr.Bahmani	1404/07/15	1404/07/17	-24	1404/07/27 15:35:33	4		
On Time	کارت برش	Mr.Bahmani	1404/07/20	1404/07/20	-7	1404/07/27 15:35:33	0		
Delayed	Data Sheet نتایج کنترل ابعادی	Mr.Bahmani	1404/07/15		-12	1404/07/27 15:35:33	12		جلسه فوری
Delayed	نقشه داخلی	Mr.Bahmani	1404/07/20		-7	1404/07/27 15:35:33	7		جلسه فوری
Delayed	نقشه دو بعدی میانی و انتهایی	Mr.Bahmani	1404/07/07	1404/07/08	-20	1404/07/27 15:35:33	1		
On Time	طرح بسته‌بندی	Mr.Ghasem nejad	1404/06/30	1404/06/30	-28	1404/07/27 15:35:33	0		
In Progress	CP	Mr.Haji	1404/08/12		15	1404/07/27 15:35:33	0		
In Progress	CP	Mr.Haji	1404/08/14		17	1404/07/27 15:35:33	0		
In Progress	CP-RW	Mr.Haji	1404/08/14		17	1404/07/27 15:35:33	0		

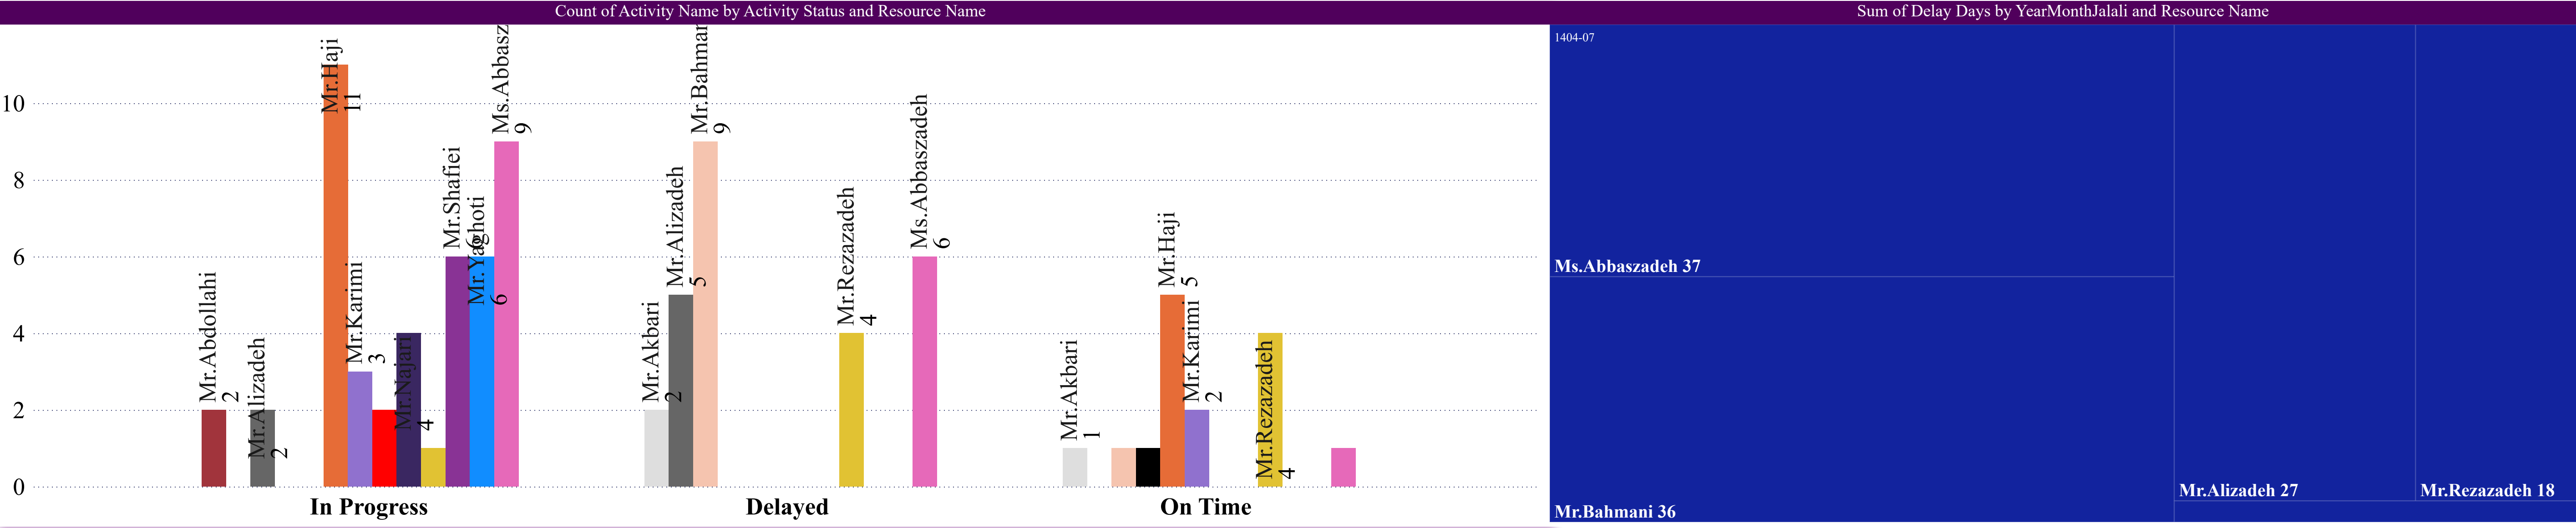

Count of Urgent by Resource Name

